

	ICS Weekly Project Report April 30, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

High School

- Ⓡ Completed week ending Friday, April 30, 2021
 - 11-month warranty walk through was conducted for the areas that were substantially complete in April/May of 2020.
 - ICS, Wold, and contractors met to review outstanding Commissioning Log.
 - Testing, balancing, and commissioning of HVAC system continued
- Ⓡ Planned week ending Friday, May 7, 2021
 - Continue to test, balance, and commission the HVAC system.

Centennial Elementary

- Ⓡ Completed week ending Friday, April 30, 2021
 - Contractors continued to address items noted on the IEA Commissioning Log.
- Ⓡ Planned week ending Friday, May 7, 2021
 - Contractors to continue to address items noted on the IEA Commissioning Log.
 - IEA Commissioning to continue verifying completed Commissioning Log items.

Sheridan Hills Elementary

- Ⓡ Completed week ending Friday, April 30, 2021
 - Completed the face brick at the Kitchen/Receiving addition.
 - Continued the installation of the controls for the new chiller unit.
- Ⓡ Planned week ending Friday, May 7, 2021
 - Continue the installation of the controls for the new chiller unit.
 - Begin flushing and filling of the new chiller system piping.

Middle School

- Ⓡ Completed week ending Friday, April 30, 2021
 - Continued design of the Best Buy Teen Tech Center
 - Sheetrock, taping, and mudding continued in the administration reception space
 - Wood shop equipment was delivered and placed

	ICS Weekly Project Report April 30, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Ⓡ Planned week ending Friday, May 7, 2021

- Continue Best Buy Tech Teen Center Design
- Paint walls and install ceiling grid in the new administration offices

STEM

Ⓡ Completed week ending Friday, April 30, 2021

- Fencing around the mechanical condensing unit continued

Ⓡ Planned week ending Friday, May 7, 2021

- Install gate and finish fence around the mechanical condensing unit

Central Ed.

Ⓡ Completed week ending Friday, April 30, 2021

- Continued mechanical and electrical rough-in in the Admin space and Area D Offices.
- Continued drywall installation in the Admin space and Area D Offices.
- Began taping and sanding drywall in the Admin space and Area D Offices.
- Began plaster patching existing plaster walls.
- Completed Roof Level mechanical curbs and openings for new mechanical equipment.
- Completed floor leveling and moisture mitigation in the Area D Offices.
- Formed and poured new concrete mechanical housekeeping pads throughout.

Ⓡ Planned week ending Friday, May 7, 2021

- Continue mechanical and electrical rough-in in the Admin space and Area D Offices.
- Complete taping and sanding drywall in the Admin space and Area D Offices.
- Begin tile installation in the Admin space and Multi-user Toilet Rooms.
- Begin painting walls in the Admin space and Area D Offices.

	ICS Weekly Project Report April 30, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

CURRENT PROJECT PHOTOS
 STEM -Fencing around HVAC condensing equipment



Middle School – Wood Shop Equipment Delivered and Placed



Middle School – Reception Space Sheet Rock, Tape, and Mudding




	ICS Weekly Project Report April 30, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan – Face brick installation progress at the Kitchen/Receiving addition.



Central Ed. – Tile backer board installation completed in the Area A Multi-user Toilet Rooms.

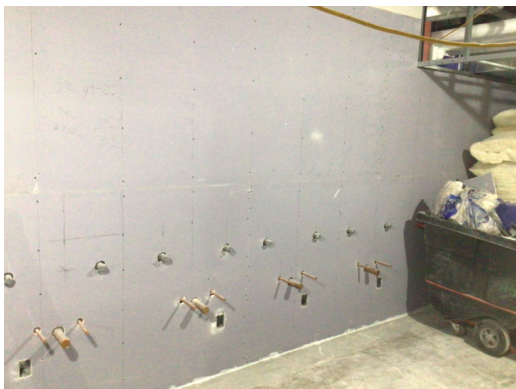

Central Ed. – Admin area drywall taping in progress.



	ICS Weekly Project Report April 30, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Central Ed. – Area D Offices floor leveling/moisture mitigation completed, drywall finishing in progress.



Central Ed. – Formed and poured new concrete mechanical equipment housekeeping pads.

