

	ICS Weekly Project Report September 24, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills Elementary

- Ⓡ Completed week ending Friday, September 24, 2021
 - Passed all final inspections in the Kitchen/Receiving areas, full use of the spaces has been granted by the authorities having jurisdiction.
 - Kitchen Staff continued moving into the new Kitchen space.
 - Installed trash enclosure swing gates.
 - Installed Gym exit stair handrails.
 - Continued HVAC/mechanical systems testing and balancing.
- Ⓡ Planned week ending Friday, October 1, 2021
 - Contractors to continue addressing punchlist items.
 - Continue testing and balancing of the HVAC/mechanical systems.
 - IEA to resume commissioning of the HVAC/mechanical systems.

Middle School

- Ⓡ Completed week ending Friday, September 24, 2021
 - Insulated auditorium HVAC hydronic re-piping
 - Started up boilers
 - Removed old building signage on canopy
 - Electrical floor outlets installed in Best Buy Teen Tech Center
 - Installed back ordered floor and wall tile in loading dock bathrooms
- Ⓡ Planned week ending Friday, October 1, 2021
 - Install doors in Best Buy Teen Tech Center
 - Reinstall ceilings in auditorium space
 - Patch and repair canopy face where signage was removed
 - Conduct training on boilers
 - Clean and turnover loading dock bathrooms

Central

- Ⓡ Completed week ending Friday, September 24, 2021
 - Completed plumbing connections to the Prep room toy washer.
 - Continued plumbing and hydronic piping in the lower-level mechanical spaces.
 - Started flushing and filling the hydronic system piping.

	ICS Weekly Project Report September 24, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Contractors continued addressing punchlist items.
- Installed rubber wall base throughout the building.
- Conducted fire alarm, mobile radio signal booster and lighting controls training with building staff and facilities personnel.
- All-State completed surveillance camera aiming and programming.

Ⓡ Planned week ending Friday, October 1, 2021

- Contractors to continue addressing punchlist items.
- All-State to conduct training on visitor management system with building staff and facilities.
- Continue plumbing and hydronic piping and insulation in the lower-level mechanical spaces.
- Conduct chiller unit start-up and Owner training.
- Install new interior room signage.

	ICS Weekly Project Report September 24, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

CURRENT PROJECT PHOTOS

Middle School – Loading Dock Bathroom Final Floor and Wall Tile Installation



Middle School – Auditorium HVAC Re-piping Insulation and Ceiling Tile Installation



Middle School – Canopy Signage Removal and Best Buy Electrical Cover Installation




	ICS Weekly Project Report September 24, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills – Kitchen/Receiving area completed. Staff move-in in-progress.



Sheridan Hills – Trash enclosure swing gates and Gym exit stair handrails installed.

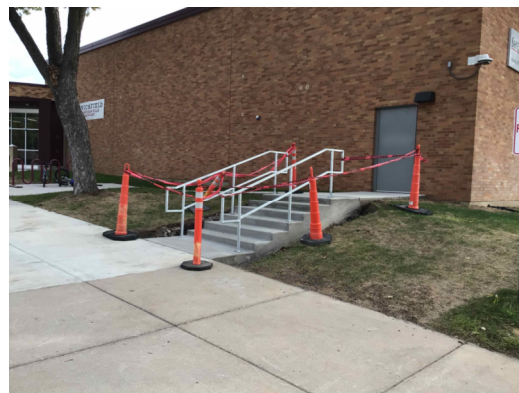



ICS Weekly Project Report

September 24, 2021



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

Central Ed. – Continued plumbing and mechanical piping in the lower-level mechanical spaces.

