





	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423



## High School

-  Completed week ending Friday, February 19, 2021
  - Delivery of interior vestibule doors at the main gym entrance, and start of installation
  - Contractors continued punch list items as well as ICS verification of completion of the punch list items.
  - Continued testing, balancing, and commissioning
-  Planned week ending Friday, February 26, 2021
  - ICS Commissioning will be on-site to review open commissioning list items for completion.
  - Contractors to continue working to address items noted on the commissioning corrective action log.

## Centennial Elementary

-  Completed week ending Friday, February 19, 2021
  - IEA Commissioning to continue commissioning the mechanical/HVAC systems.
  - Contractors continued working IEA Commissioning log items.
-  Planned week ending Friday, February 26, 2021
  - IEA Commissioning to continue commissioning the mechanical/HVAC systems.
  - Contractors to continue working to address IEA Commissioning log items.

## Sheridan Hills Elementary

-  Completed week ending Friday, February 19, 2021
  - IEA Commissioning continued the commissioning of the mechanical/HVAC systems.
  - Contractors continued working to address punch list and IEA Commissioning log items.
-  Planned week ending Friday, February 26, 2021
  - IEA Commissioning to continue commissioning the mechanical/HVAC systems.
  - Contractors to continue to address punch list and IEA Commissioning log items.

	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## Middle School

### Ⓡ Completed week ending Friday, February 19, 2021

- General
  - Short power outage for electrical connections
- Third Floor Restrooms
  - Turned over to school
- Second Floor Restrooms
  - Punch list
  - Final cleaned
- First Floor Restrooms
  - Sheet rocked north bathrooms
  - Started tiling in south bathrooms
- Existing Administration Offices/New Special Education Suite
  - Continued painting
  - Continued ceiling grid
  - Finished soffits in corridor
- Existing Music Suite/New Design Lab
  - Carpeted band room
  - Continued mechanical and electrical rough ins
- Wood Shop/New Administration/Fab Lab
  - Continued mechanical rough ins
  - Continued wall framing

### Ⓡ Planned week ending Friday, February 26, 2021

- Second Floor Restrooms
  - Turn over to school
- First Floor Restrooms
  - Start tiling north restrooms
  - Finish tiling south restrooms
  - Start installing toilet fixtures and toilet partitions in south restrooms
- Existing Administration Offices/New Special Education Suite
  - Finish ceilings
- Existing Music Suite/New Design Lab
  - Install floor insulation at tiered music room

	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Pour concrete floor in music room
- Continue mechanical and electrical rough ins
- Wood Shop/New Administration/Fab Lab
  - Finish wall framing
  - Start sheet rocking
  - Continue mechanical electrical rough ins

#### STEM

- Ⓡ Completed week ending Friday, February 19, 2021
  - Review operation and maintenance manuals
- Ⓡ Planned week ending Friday, February 26, 2021
  - ICS to continue commissioning

#### Dual Language

- Ⓡ Completed week ending Friday, February 19, 2021
  - Contractors continued working to address items noted on the commissioning corrective action log.
- Ⓡ Planned week ending Friday, February 26, 2021
  - ICS Commissioning will be on-site to review open commissioning list items for completion.
  - Contractors to continue working to address items noted on the commissioning corrective action log.

#### Central Ed.

- Ⓡ Completed week ending Friday, February 19, 2021
  - Material submittals are being uploaded to Procore for review and approval.
  - Conducted the weekly Construction Progress/Coordination meeting.
  - All Furniture (moving coming) completed the move-out of district items out of the Phase 1 construction area.
  - District IT facilitated moving staff technology components out of the Phase 1 construction area to their temporary office locations.

	<b>ICS Weekly Project Report</b> February 19, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Ⓡ Planned week ending Friday, February 26, 2021

- Continue with weekly Construction Progress/Coordination meetings.
- Continue receiving and reviewing material submittals.
- Rochon (General Contractor) to mobilize on-site and construct temporary partitions and begin demolition.
- Abatement contractor to mobilize on-site to setup containment areas and begin their material removals.



	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

CURRENT PROJECT PHOTOS  
 Middle School – Main Level Boys and Girls Bathroom Progress



Middle School – New Admin/Nurse Wall Framing and Mechanical/Electrical Rough Ins



	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – New Special Education/Old Administration Offices-Painted and Ceilngs Installed







	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Main Level Corridor Outside Special Education Ceiling and Soffits Completed



Middle School – (Music Suite) Band Room Carpeted and Design Lab Mechanical Rough Ins

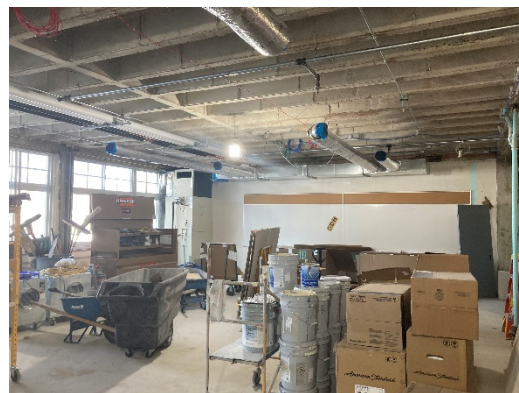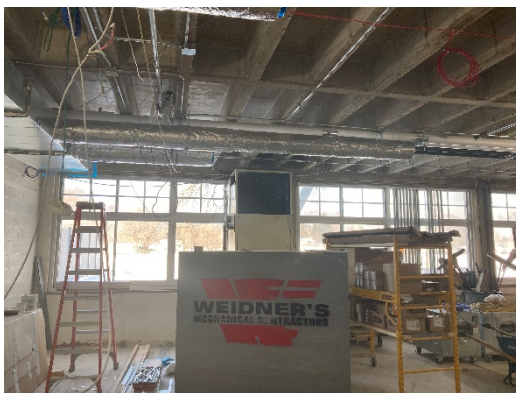

	<b>ICS Weekly Project Report</b> February 19, 2021
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

### High School – Athletic Door Vestibule Installation



### Central Ed. – Completed move-out/relocation of staff furniture and technology from Phase 1 construction areas.

